

C St NE Implementation
DC CONTRACT NO. DCKA-2020-C-0056
FAP No.: CM-2020 (018)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

01/17/2022 – 01/21/2022

Project Website: www.cstne.com



© Jan 19, 2022 401 Oklahoma Ave NE, Washington DC 20002, US

C St NE Project Lay Down Yard – Delivery of Light Poles

1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17th, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on April 26th, 2021 and a substantial completion date of September 28th, 2022

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on February 12th, 2021 that will expire on October 15th, 2022.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, January 17th, 2022 thru date January 21st, 2022. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, Anchor Construction, WGL, creating and revising meeting minutes, reviewing IDR's, reviewing design plans, reviewing specifications, reviewing RFI's, reviewing submittals, reviewing the monthly schedule update, updating submittal and RFI logs, reviewing quantities, drafting correspondence on DDOT's behalf, and answering various DDOT and Contractor queries.

The Contractor performed the following construction activities this week.

Monday 01/17/2022 – DDOT Holiday – No Work Performed

Tuesday 01/18/2022

CM

- Verified & inspected Contractor work activities and tested concrete

Contractor

- C St NE & 18th PL – Alfaro
 - Excavate, install conduit, and place concrete between M47 and M49
- C St NE & 19th – Anchor
 - Sawcut Phase 1F
 - Excavate and demo median (phase 1F)
 - Compact subgrade, place GAB and compact
- C St NE & 20th – Alfaro
 - Excavate, install conduit, and place concrete between M58 and M61

Wednesday 01/19/2022

CM

- Verified & inspected Contractor work activities



Contractor

- C St NE & 18th PL – Alfaro
 - Backfill between M47 and M49 with RC-6
- C St NE & 19th – Anchor
 - Place GAB and compact – compaction testing failed
 - Prep area for PCC Base
- C St NE & 20th – Alfaro
 - Backfill between M58 and M61 with RC-6

Thursday 01/20/2022

CM

- Created IDR's, reviewed contract documents, plans, and submittals

Contractor

- Cancelled work due to inclement weather

Friday 01/21/2022

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 18th – Alfaro
 - Patch deteriorated asphalt above duct bank trenches
- C St NE & 19th – Anchor
 - DDOT QA inspect subgrade – remove GAB and undercut 12 inches
- C St NE & 19th – Alfaro
 - Patch deteriorated asphalt above duct bank trenches
- C St NE & 20th – Alfaro
 - Patch deteriorated asphalt above duct bank trenches
- C St NE & 21st – Alfaro
 - Patch deteriorated asphalt above duct bank trenches

3. PHOTOS OF WORK PERFORMED THIS PERIOD


Monday 01/17/2022 – DDOT Holiday – No Work Performed	
Tuesday 01/18/2022	



C St NE & 19th – Anchor
Sawcut Phase 1F



C St NE & 19th – Anchor
Excavate and demo median (phase 1F)

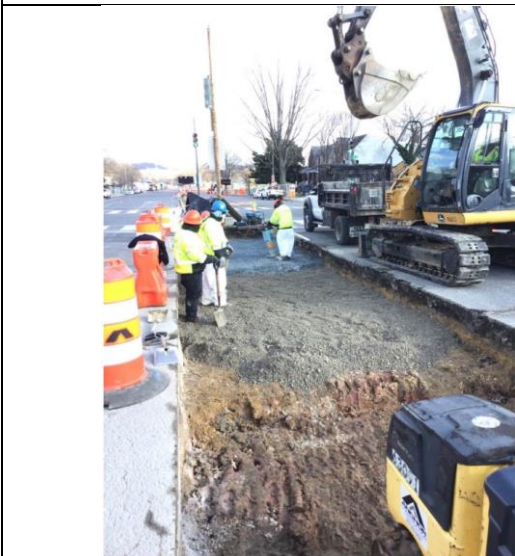

C St NE & 19th – Anchor
Compact subgrade, place GAB and compact




C St NE & 18th PL – Alfaro
Excavate, install conduit, and place concrete between M47 and M49



© Jan 18, 2022 2009-2011 C St NE, Washington DC 20002, US

C St NE & 20th – Alfaro
Excavate, install conduit, and place concrete between M58 and M61



Wednesday 01/19/2022



C St NE & 19th – Anchor
Place GAB and compact – compaction testing failed



C St NE & 19th – Anchor
Prep area for PCC Base





© Jan 19, 2022 1890 C St NE, Washington DC 20002, US

C St NE & 18th PL – Alfaro
Backfill between M47 and M49 with RC-6



© Jan 19, 2022 2013-2018 C St NE, Washington DC 20002, US

C St NE & 20th – Alfaro
Backfill between M58 and M61 with RC-6

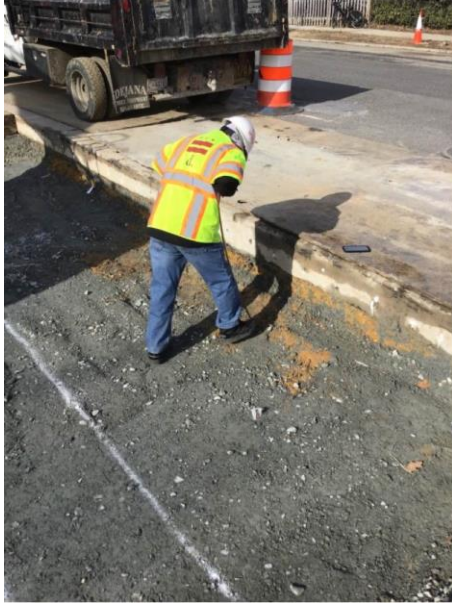Thursday 01/20/2022 – Work Cancelled due to Inclement Weather	
Friday 01/21/2022	
	
<p>C St NE & 19th – Anchor DDOT QA inspect subgrade – remove GAB and undercut 12 inches</p>	<p>C St NE & 19th – Alfaro Patch deteriorated asphalt above duct bank trenches</p>
