



C St NE Implementation
DC CONTRACT NO. DCKA-2020-C-0056
FAP No.: CM-2020 (018)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

09/06/2021 – 09/10/2021

Project Website: www.cstne.com

1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17th, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on April 26th, 2021 and a substantial completion date of September 28th, 2022

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on February 12th, 2021 that will expire on October 15th, 2022.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, September 6th, 2021 thru date September 10th, 2021. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, Anchor Construction, WGL, creating and revising meeting minutes, reviewing IDR's, reviewing design plans, reviewing specifications, reviewing RFI's, reviewing submittals, updating submittal and RFI logs, reviewing quantities, drafting correspondence on DDOT's behalf, and answering various DDOT and Contractor queries.

The Contractor performed the following construction activities this week.

Monday 09/06/2021 – no work due to Labor Day Holiday

CM

Contractor

Tuesday 09/07/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Backfill 15" RCP with RC-6 between M6-10 and I7-3
- C St NE & 21st – Anchor
 - Excavate for 15" RCP between M8-5 and I8-5

Wednesday 09/08/2021

CM

- Verified & inspected Contractor work activities and tested concrete

Contractor

- C St NE & 19th – S&J
 - Excavate for 15" RCP between M6-10 and I7-3
- C St NE 2000 Block - Anchor
 - Saw cut for M8-2
- C St NE & 21st – Anchor
 - Place 15" RCP and concrete cradle between M8-5 and I8-5

Thursday 09/09/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Excavate and place 15" RCP between M6-10 and I7-3
- C St NE 2000 Block - Anchor
 - Test Pit for electrical line between M8-2 and I7-15

Friday 09/10/2021

CM

- Verified & inspected Contractor work activities


Contractor

- C St NE & 19th – S&J
 - Excavate and place 15" RCP between M6-10 and I7-3
- C St NE & 21st – Anchor
 - Backfill 15" RCP with RC-6 between M8-5 and I8-5

4. PHOTOS OF WORK PERFORMED THIS PERIOD



© Sep 7, 2021, 229-21st St NE, Washington DC 20002, US
C St NE & 21st St – Excavate 15" RCP between M8-5 to I8-5

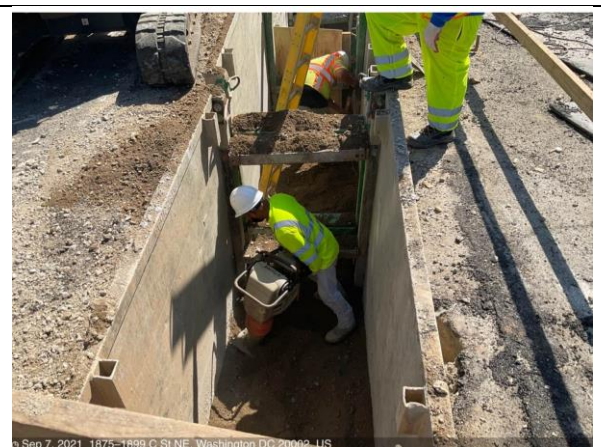

© Sep 7, 2021, 1875-1899 C St NE, Washington DC 20003, US
C St NE & 19th St – Backfill 15" RCP between M6-10 to I7-3




© Sep 8, 2021 22nd St NE, Washington DC 20002, US

C St NE & 21st St – Concrete for 15" RCP between M8-5 to I8-5




© Sep 8, 2021 2043-2069 C St NE, Washington DC 20002, US

C St NE 2000 Block – Saw cut for M8-2

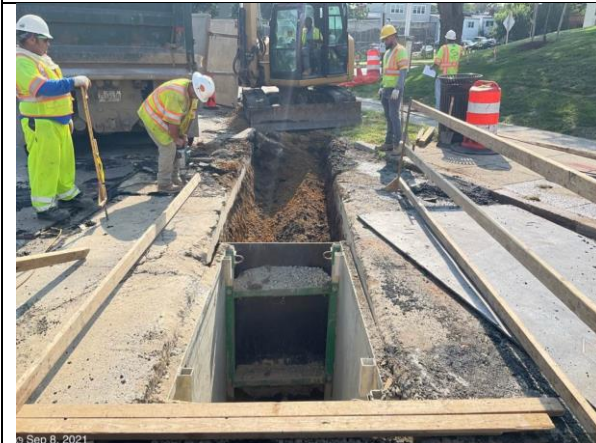


© Sep 8, 2021

C St NE & 19th St – Excavate 15" RCP between M6-10 to I7-3

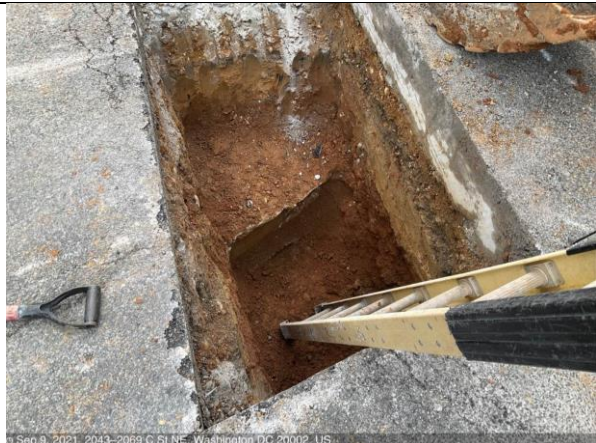

© Sep 9, 2021 2043-2069 C St NE, Washington DC 20002, US

C St NE 2000 Block – Test Pit cut between M8-2 and I7-15

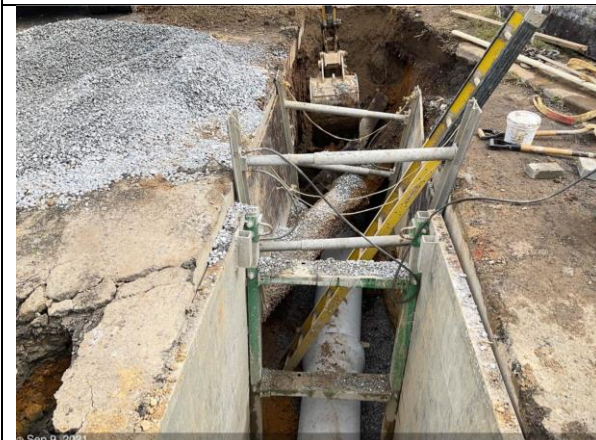

© Sep 9, 2021

C St NE & 19th St – Excavate and place 15" RCP between M6-10 to I7-3



© Sep 10, 2021 22nd St NE, Washington DC 20002, US

C St NE & 21st St – Backfill 15" RCP between M8-5 to I8-5



<p>C St NE & 19th St – Excavate and place 15" RCP between M6-10 to I7-3</p>	
