



Project Office
RFK Stadium Lot 6

C St NE Implementation
DC CONTRACT NO. DCKA-2020-C-0056
FAP No.: CM-2020 (018)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

09/13/2021 – 09/17/2021

Project Website: www.cstne.com

1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17th, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on April 26th, 2021 and a substantial completion date of September 28th, 2022

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on February 12th, 2021 that will expire on October 15th, 2022.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, September 13th, 2021 thru date September 17th, 2021. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, Anchor Construction, WGL, creating and revising meeting minutes, reviewing IDR's, reviewing design plans, reviewing specifications, reviewing RFI's, reviewing submittals, updating submittal and RFI logs, reviewing quantities, drafting correspondence on DDOT's behalf, and answering various DDOT and Contractor queries.

The Contractor performed the following construction activities this week.

Monday 09/13/2021

CM

- Verified & inspected Contractor work activities and tested concrete

Contractor

- C St NE & 19th – S&J
 - Place concrete for 15" RCP cradle between M6-10 and I7-3
- C St NE & 17th – Anchor
 - Install tree protection (2)
- C St NE & 21st – Anchor
 - Test pit for PEPCO facility between M8-2 and I8-2

Tuesday 09/14/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Backfill 15" RCP with RC-6 between M6-10 and I7-3
- C St NE & 21st – Anchor
 - Test pit for utilities between M8-1 and I8-1



Wednesday 09/15/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Excavate for inlet I6-11
- C St NE & 21st – Anchor
 - Excavate for 15" RCP between M8-1 and I8-1

Thursday 09/16/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 19th – S&J
 - Install inlet I6-11
- C St NE & 18th – Anchor
 - Install tree protection (2)
- C St NE & 21st – Anchor
 - Excavate for 15" RCP between M8-1 and I8-1

Friday 09/17/2021

CM

- Verified & inspected Contractor work activities

Contractor

- C St NE & 21st – Anchor
 - Brick channel for M8-5


3. PHOTOS OF WORK PERFORMED THIS PERIOD



© Sep 13, 2021, 2043-2069 C St NE, Washington DC 20002, US
C St NE & 21st St – Test pit for PEPCO facility between M8-2 and I8-2



© Sep 13, 2021
C St NE & 19th St – Concrete cradle for 15" RCP between M6-10 to I7-3

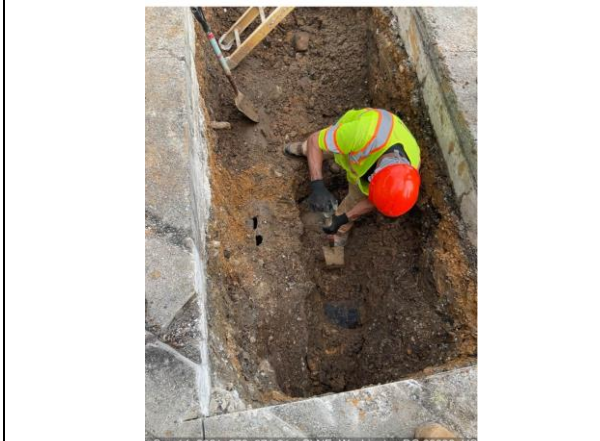

© Sep 14, 2021, 273-371 21st St NE, Washington DC 20002, US
C St NE & 22nd St – Test pit utilities between M8-1 and I8-1



© Sep 14, 2021
C St NE & 19th St – Backfill 15" RCP between M6-10 to I7-3



9 Sep 15, 2021

C St NE & 22nd St – Excavate for 15" RCP between M8-1 and I8-1



9 Sep 15, 2021

C St NE & 19th St – Excavate for I6-11




9 Sep 16, 2021 233-271 21st St NE, Washington DC 20002, US

C St NE & 22nd St – Excavate for 15" RCP between M8-1 and I8-1




9 Sep 16, 2021

C St NE & 19th St – Install I6-11

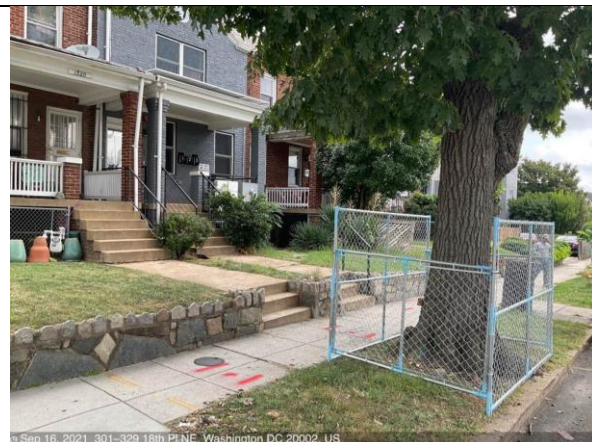

9 Sep 16, 2021 301-329 18th Pl NE, Washington DC 20002, US

C St NE & 18th St – Install Tree Protection

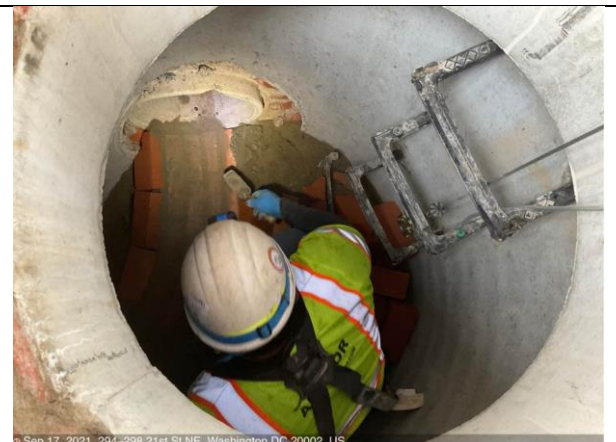

9 Sep 17, 2021 294-098 21st St NE, Washington DC 20002, US

C St NE & 21st St – Brick channel for M8-5
