



Project Office  
RFK Stadium Lot 6

**C St NE Implementation**  
**DC CONTRACT NO. DCKA-2020-C-0056**  
**FAP No.: CM-2020 (018)**

---

# **CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT**

**09/20/2021 – 09/24/2021**

---

Project Website: [www.cstne.com](http://www.cstne.com)

## 1. EXECUTIVE SUMMARY

### Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17<sup>th</sup>, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on April 26<sup>th</sup>, 2021 and a substantial completion date of September 28<sup>th</sup>, 2022

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on February 12<sup>th</sup>, 2021 that will expire on October 15<sup>th</sup>, 2022.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, September 20<sup>th</sup>, 2021 thru date September 24<sup>th</sup>, 2021. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, Anchor Construction, WGL, creating and revising meeting minutes, reviewing IDR's, reviewing design plans, reviewing specifications, reviewing RFI's, reviewing submittals, updating submittal and RFI logs, reviewing quantities, drafting correspondence on DDOT's behalf, and answering various DDOT and Contractor queries.

The Contractor performed the following construction activities this week.

### Monday 09/20/2021

#### CM

- Verified & inspected Contractor work activities

#### Contractor

- C St NE & 19<sup>th</sup> – S&J
  - Excavate, place, and backfill inlet I6-11 with RC-6
- C St NE & 18<sup>th</sup> – Anchor
  - Install tree protection (3)
- C St NE & 20<sup>th</sup> – Anchor
  - Saw cut and excavate for manhole M7-5
- C St NE & 21<sup>st</sup> – Anchor
  - Trench excavation for 15" RCP between M8-7 and M8-2 (RFI 043)

### Tuesday 09/21/2021

#### CM

- Verified & inspected Contractor work activities

#### Contractor

- C St NE & 19<sup>th</sup> – S&J
  - Excavate, for 15" RCP between inlet I6-11 and manhole M6-10



- C St NE & 20<sup>th</sup> – Anchor
  - Install rebar for M7-5 base
- C St NE & 21<sup>st</sup> – Anchor
  - Backfill 15" RCP between M8-7 and M8-2 (RFI 043) with RC-6

**Wednesday 09/22/2021**

**CM**

- Verified & inspected Contractor work activities and tested concrete

**Contractor**

- C St NE & 19<sup>th</sup> – S&J
  - Install 15" RCP between inlet I6-11 and manhole M6-10
- C St NE & 20<sup>th</sup> – Anchor
  - Place concrete for M7-5 base
- C St NE & 21<sup>st</sup> – Anchor
  - Excavate 15" RCP between M8-7 and M8-2 (RFI 043)

**Thursday 09/23/2021**

**CM**

- Completed IDR's, reviewed plans, and specifications

**Contractor**

- Cancelled work due to inclement weather

**Friday 09/24/2021**

**CM**

- Verified & inspected Contractor work activities and test concrete

**Contractor**

- C St NE & 19<sup>th</sup> – S&J
  - Place concrete cradle for 15" RCP between inlet I6-11 and manhole M6-10
- C St NE & 20<sup>th</sup> – Anchor
  - Excavate for 18" RCP between M7-5 and M7-10
- C St NE & 21<sup>st</sup> – Anchor
  - Install 15" RCP between M8-7 and M8-2 (RFI 043)

**3. PHOTOS OF WORK PERFORMED THIS PERIOD**



C St NE & 19th St – Excavate, place, and backfill inlet I6-11 with RC-6




C St NE & 20th – Saw cut and excavate for manhole M7-5



C St NE & 21st St – Trench excavation for 15" RCP between M8-7 and M8-2 (RFI 043)



C St NE & 19th – Excavate, for 15" RCP between inlet I6-11 and manhole M6-10

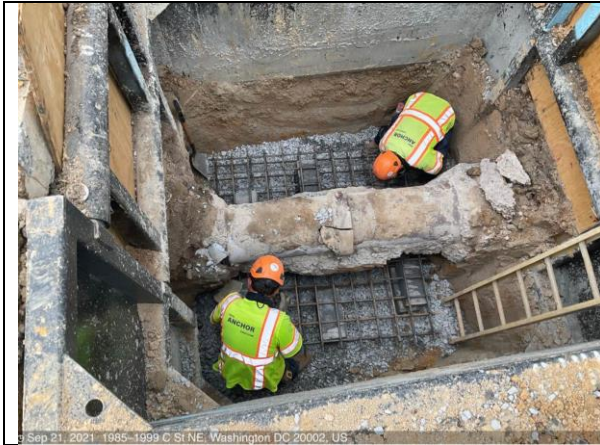

C St NE & 20th – Install rebar for M7-5 base



C St NE & 19th – Install 15" RCP between inlet I6-11 and manhole M6-10



C St NE & 20th – Place concrete for M7-5 base



C St NE & 21st – Excavate 15" RCP between M8-7 and M8-2 (RFI 043)

	
<p>C St NE &amp; 19th – Place concrete cradle for 15" RCP between inlet I6-11 and manhole M6-10</p>	<p>C St NE &amp; 20th – Excavate for 18" RCP between M7-5 and M7-10</p>
	
<p>C St NE &amp; 21st – Install 15" RCP between M8-7 and M8-2 (RFI 043)</p>	
