



Project Office
TBD

C St NE Implementation
DC CONTRACT NO. DCKA-2020-C-0056
FAP No.: CM-2020 (018)

CONSTRUCTION MANAGER'S WEEKLY PROGRESS REPORT

03/15/2021 – 03/19/2021

Project Website: www.cstne.com

Picture -Date – Description



1. EXECUTIVE SUMMARY

Project Description:

Work under this contract consists of improving the existing streetscape and safety for pedestrians and cyclists. The project plans to mill and overlay the pavement surface, reconstruct sidewalks as needed, and install bulb-outs and bus pads, crosswalks, pavement marking and wheelchair ramps. Streetlights, traffic signals and drainage structures will be upgraded. Other design elements considered for the project are LID elements and intersection improvements. The project will upgrade the bike facilities from bike lanes to protected bike lanes, add more pedestrian crossings, and ensure the street complies with the Americans with Disabilities Act (ADA).

This project is 83% Federally Funded and 17% District-Funded. DDOT selected Anchor construction corporation. as the contractor and awarded the \$15,995,763.50 contract on February 17, 2021. DDOT issued notice to proceed with contract work to Anchor construction corporation with work to begin on xx/xx/xxxx and a substantial completion date of xx/xx/xxxx.

Jacobs is providing Construction Management and Inspection services. DDOT issued a task order to Jacobs on 02/12/2021 that will expire on 10/15/2022.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Work this week was performed during the day on date, March 15, 2021 thru date March 19, 2021. Work included the CM Agent Team organizing, chairing, and participating in meetings with DDOT, the Designer (Volkert), Anchor Construction, and Washington Gas, creating and revising meeting minutes, reviewing the Safe Accommodation Law and how it applies to the C St NE design, providing a list of plan quantity discrepancies and requested clarifications to Volkert, developing the project web site and handouts, coordinating with Turner Contracting regarding the Eliot-Hine Middle School, developing a submittal register, documenting onsite conditions, updating procedures, reviewing design plans, and answering various DDOT queries.

No Contractor work took place this week.

Monday 03/15/2021:

Contractor

- At #####
 -

Tuesday 03/16/2021

CM

- Washington Gas continued installation of main pipe and service branches on C St NE between 15 St and 16 St NE.
- Pre-construction pictures were taken.

Contractor

- At/Along ### (various locations)
 -

Wednesday 03/17/2021

CM



- Washington Gas crew continued working on C St NE between 16 St and 17 St NE on eastbound and westbound direction
- Verizon were installing the 4 inches PVC conduit for communication line on C St NE and 20 St NE
- Pre-construction pictures were taken.

Contractor

- At/Along (various locations)
 -

Thursday 03/18/2021

CM

- Washington Gas and Verizon were not onsite due to weather
- Pre-construction pictures were taken.

Contractor

- At/Along ...
 - ...

Friday 03/19/2021

CM

- Washington Gas continued working on C St NE between 15th & 17th Street NE in the middle lanes on service connections.
- Mighty Four, a WGL sub, was restoring roadway on 17th Street
- JJB, Verizon's sub, installed 4" PVC on 20th Street from South to North.
- Pre-construction pictures were taken.

Contractor

- At/Along ...
 - ...

Contractor

- Along/At ... (various locations)
 -

3. PHOTOS OF WORK PERFORMED THIS PERIOD



Picture No. 1: 03162021 – WGL relocation, C St NE & 16th looking east



Picture No. 2: 03172021 – WGL Services C St NE at 14th, looking west



Picture No. 3 – 03182021 – Existing Conditions C St NE at 18th, looking west




Picture No. 4 – 03182021 – Verizon relocation, C St NE at 20th, looking west



Picture No. 5 – 03192021 – WGL Services, C St NE at 15th, looking east



Picture No. 6 – 03192021 – Pavement restoration by Mighty Four, WGL sub, C St NE and 17th St PI looking south

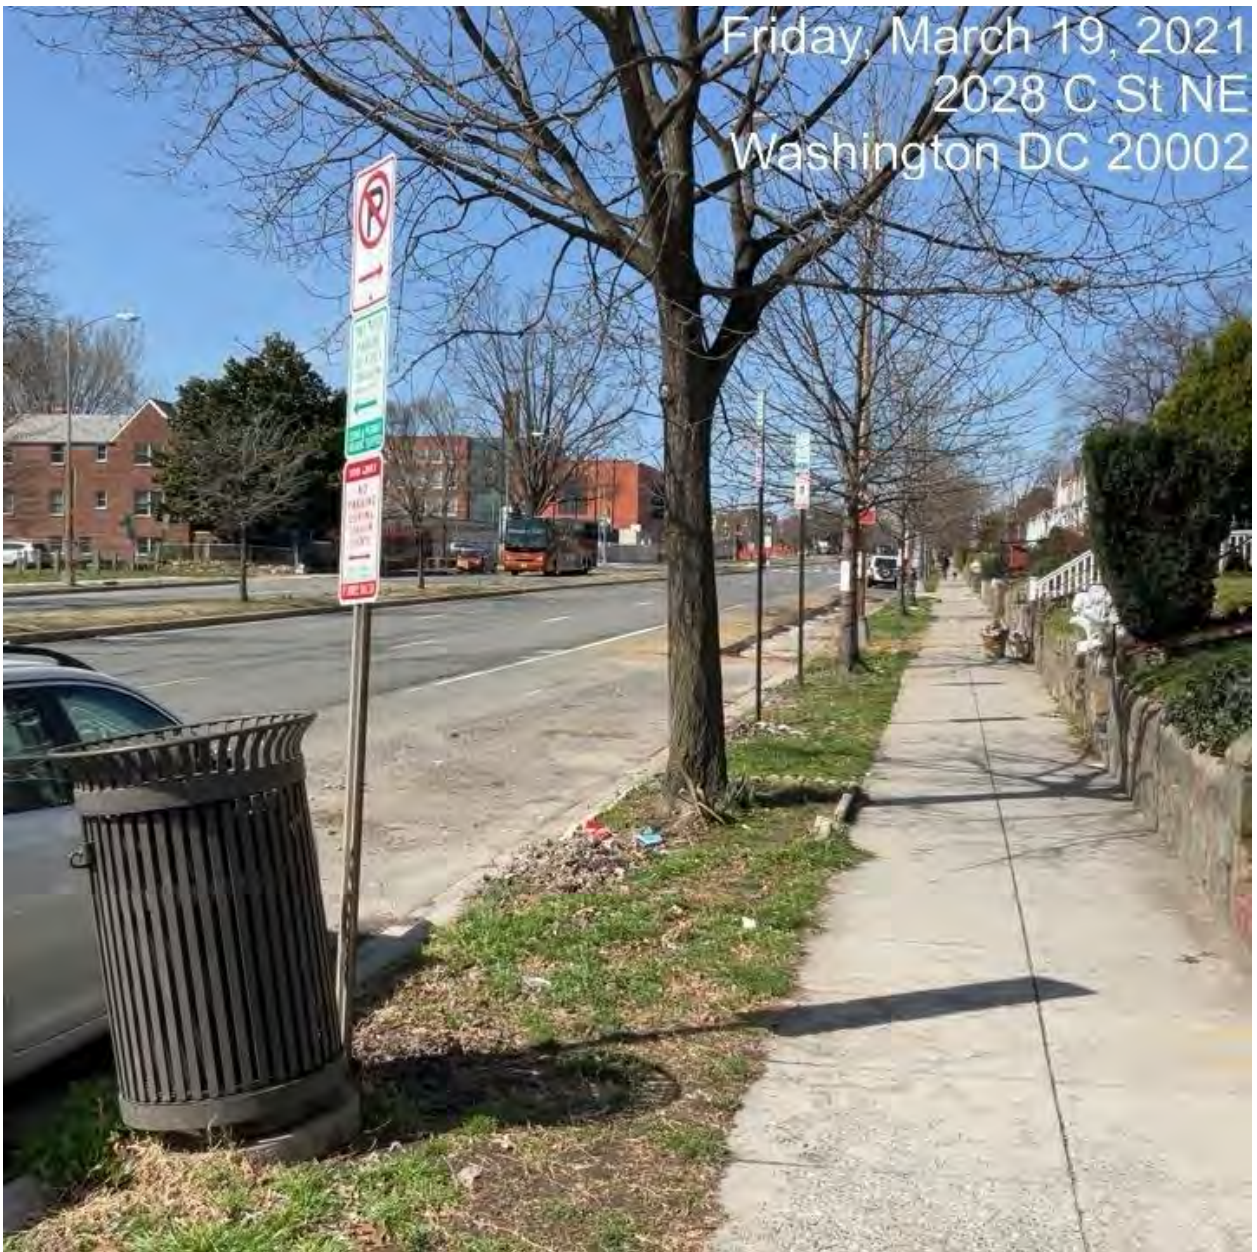

Picture No. 7 – 03192021 – Existing Conditions, C St NE at 20th, looking west
